

Magnetic Particle Inspection Certificate

Mag Number: 34310
Inspection Date: 1/30/2015
Customer: Giant Power Tongs
Inspector: David Villareal
Inspector's Level: Level II per ASNT-TC-1A

COPY

**Test Equipment Information*

Model: 1105-8
Control number: G6P6000
Serial Number: 1105-8
Wet - Fluorescent - AC

Part Information

Part Number: T43950-141
Part Description: TI MFG 9-5/8" 250 SLX SIDE DOOR
ELEVATOR - NEW WITH MPI & LOAD TEST
Manufacturer: Texas International
Order Number/Line Item: 23559-01
Article: 1 of 2 **A**
Observations: No Visible Signs of Defect were found.
40618
formerly 22265-03

Signed:

A handwritten signature in black ink, appearing to be 'David Villareal', written over a horizontal line.



PROOF OF LOAD


Date: December 16, 2014

Time: 3:40 PM

Inspector	Work Order # /Line Item	Part Number	Serial	LT #	Hold Time	Test Load
BRowe	22003-07	T43950-141	40618	141235LT	5 minutes	375 Tons

Product Description	9 5/8" 250 Ton SLX Side Door Elevator					
Special Conditions – Customer's test request conditions that do <u>not</u> meet API or manufacturer's load rating original specification	COPY					

CHART

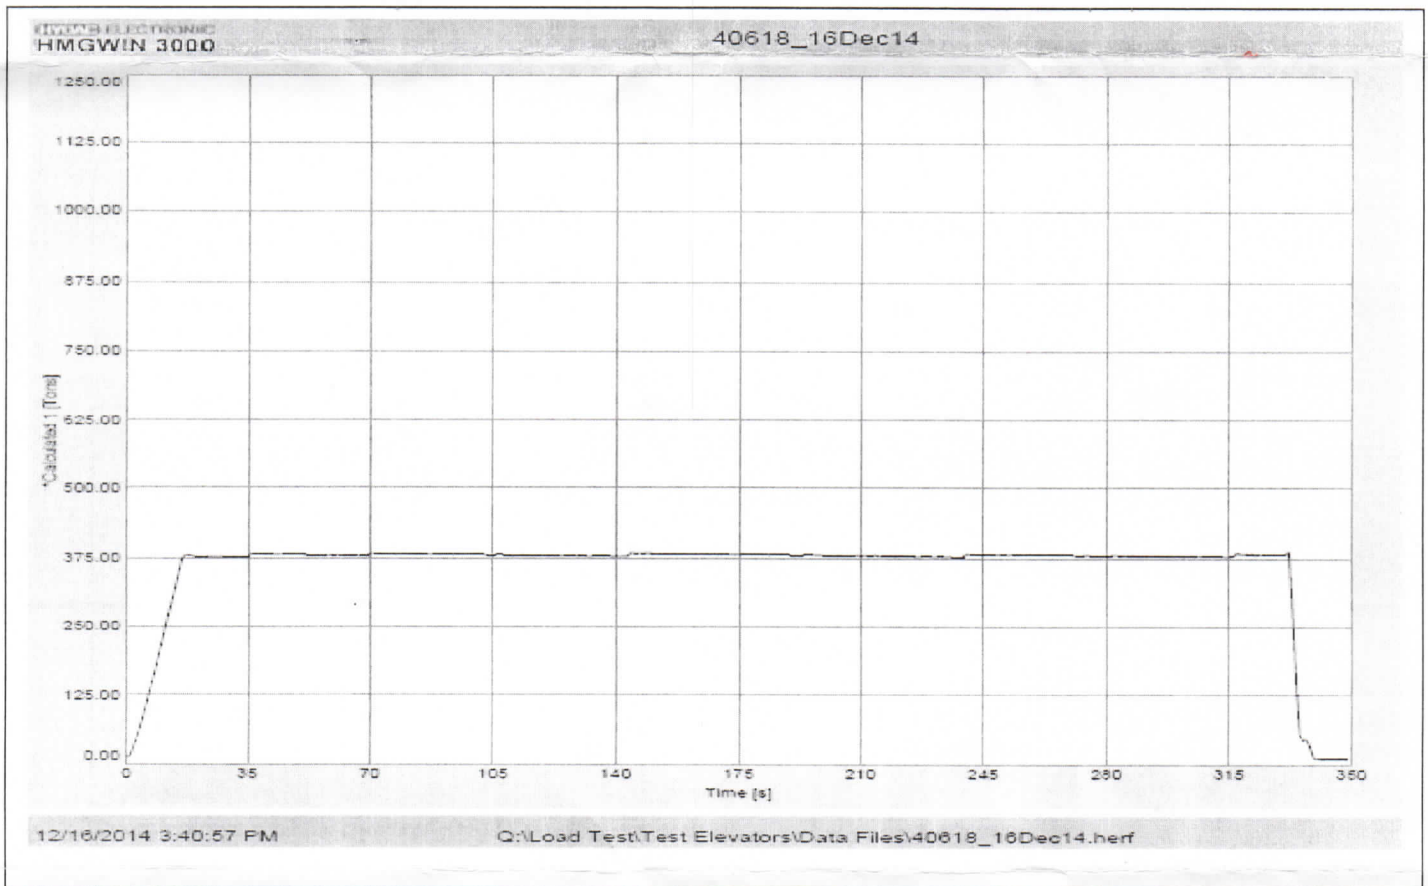

Rating -Tons	Pressure -Bar	Load -Tons
75	62	112
150	125	225
250	207	375
350	290	525
500	414	750

Load test unit is calibrated according to ASTM E4. Nondestructive testing shall be performed 24 hours after load test to determine product condition. Load test results are a confirmation of load applied as indicated in test protocol. Certification of load only applies to rated load of elevator tested in conformance to API and manufacturer load specification. *Customer is responsible for the proper installation and use of the equipment.*
